

The Live View (v6 features)


Phasing Conception

In few words


The Live view allows you to create 2D representations of your project and to export them in video.

Access

Access to the Live View from the Create phasing tab.

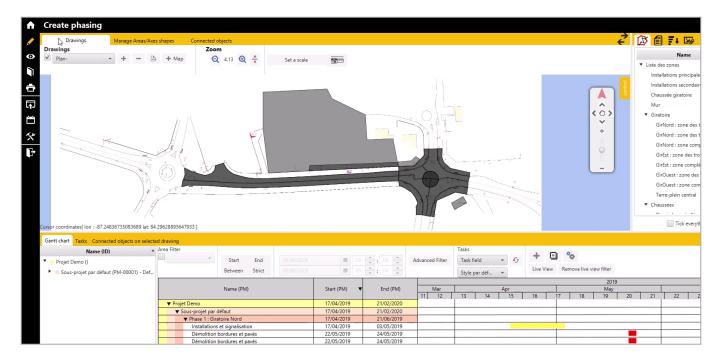



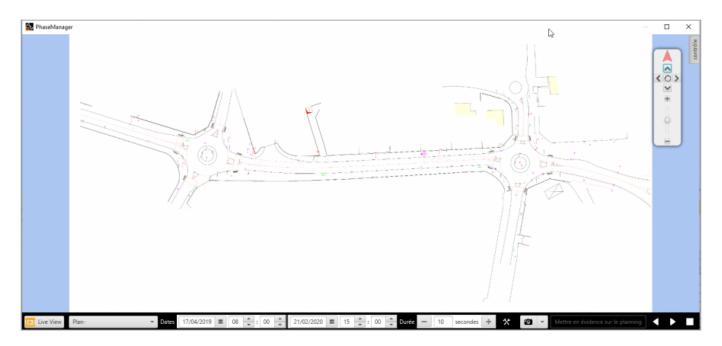

Play your project

Visualize you project by clicking on the Play button ► in the bottom right corner. Moodify the dates to choose a specific moment. You can also modify the duration. Diplay another drawing or printed zone with the dropdown list in the left.

Plan- 🔹 Dates 17/04/2019 🔳 08 💠 : 00 💠 21/02/2020 🖩 15 💠 : 00 💠 Durée - 10 secondes 🛨 🛠 🔯 🔹 Mettre en évidence sur le planning 🔍 🕨

Gantt

The Live view is open in another window than Phase Manager. So you can see your Gantt in Phase Manager in the same time (It's recommended to have 2 screens). Once the Live View is open, a cursor will appear in your Gantt. Its size corresponds to the time interval for the period displayed on the Live View, and its location corresponds to the dates of this period. It is possible to change the time interval and cursor location manually. However, during the video playing, the cursor will take over the parameters entered. The filters entered in your Gantt are also applied in Live View.

Settings


Viewing

You can change Live View settings via the Settings button . This window allows you to configure the objects/annotations to be displayed during Live view playing, as well as the time interval for it.

😵 Configuration live view	— 🗆 X
Affichage Titrage	
Intervalle de temps : Journées 🔹	
Afficher les emprises sur les axes	 Afficher les zones/axes commencés Afficher les zones/axes à faire Afficher les zones/axes terminés
 ✓ Afficher les annotations Police : System Couleur du texte : #f2f2f2 ▼ Coulour 	leur de fond : 📕 #334db3 👻
	OK Annuler

Titling

The Titling tab lets you display the name of the subproject during playback.

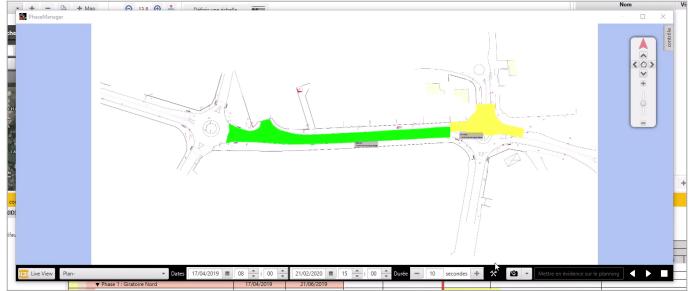

Capture


Pause playback and take a screenshot of your phasing at a specific moment by clicking the button

Highlight on the schedule

Pause while playing and highlight the relevant activities at that moment in your Gantt. A filter will be automatically created in the Gantt.


÷Ô

To deactivate the filter, from the Phase Manager window, click on the Remove Live View filter button.

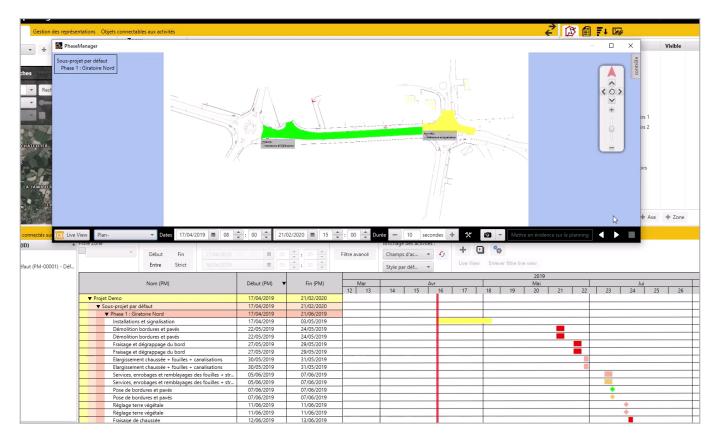

Studio Mode

Click the button on the left to switch to Studio mode. The Studio mode allows you to visualize your project on different drawings at different times of it.



Add a drawing or a print area

Click the Add print area button and choose the desired print plan or area. Configure each plan by clicking on it and modifying the dates and/or duration.





Transition

Add a transition by clicking on a the bar representing your drawing. You will be able to modify the Before and After transition if a drawing is present before or after the selected one. You can also decrease or increase the duration of the transition by moving the cursor directly over the transition representation.

															×
🗱 PhaseManager								_							~
		No Ne			I , ,										control
📔 Studio Nouveau montage1 👻 + - 🕒 Plan-	• Dates 15/04/2	019 🖩 08 🍝 :	00 20/0	5/2019 🔳 23 🔆	★ : 59 ★ Du	uration –	- 10 second	ds 🕇 🛠	Trai	nsition 6		jht on the s	_	Move th.	
05 - 15/04/2019	00:05	ι.		00:10			e		00:15						00:2
05 - 15/04/2019															
 15/04/2019 15/04/2019 	Plan-		1 1 1	20/05/2019 17/04 Move then z	4/2019	. 1. 1	I S., I I	s Plan-	Printed zo	ne	-1 - I		1 (31	0/09/2019
15/04/2019	Plan-			20/05/2019 17/04	4/2019		I I I I			ine	1 1			3	0/09/2019
15/04/2819				20/05/2019 17/04 Move then z	•			2019		ne -	1	· · · ·			
15/04/2019	Plan- Start (PM) ■	End (PM)	Mar	20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo			un			Jul
ISJON/2019 Detercer Name (PM)	Start (PM)		Mar 11 12	20/05/2019 17/04 Move then z	•	17		2019		ne 22	J 	un 24	25		
IS/04/2819	Start (PM) 17/04/2019	21/02/2020		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
ISJON/2015 ISJON/2015 Image: Source of the second seco	Start (PM) 17/04/2019 17/04/2019	21/02/2020 21/02/2020		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Isynkyzets Isynkyzets Name (PM) ▼ Projet Demo ▼ Sous-projet par défaut ▼ Phase 1: Giratoire Nord	Start (PM) 17/04/2019 17/04/2019 17/04/2019	21/02/2020 21/02/2020 21/06/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Image: Source and Source a	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019		20/05/2019 17/04 Move then z	Apr	17		2019 May	Printed zo				25		Jul
Isylwazens Isylwazens Name (PM) ▼ Projet Demo ▼ Sous-projet par defaut ▼ Phase 1 : Giratoire Nord Installatione et signalisation Demolition bordnese et pavés	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 17/04/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Image: Source of the second secon	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019		20/05/2019 17/04 Move then z	Apr	17		2019 May	Printed zo				25		Jul
Image: Source and Source a	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 27/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019 29/05/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Isymuzzens Isymuzzens Name (PM) ▼ Projet Demo ▼ Sous-projet par défaut ▼ Phase 1: Giratoire Nord Installations et signalisation Démolition bordures et pavés Démolition bordures et pavés Fraisage et dégrappage du bord Fraisage et dégrappage du bord	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 27/05/2019 27/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019 29/05/2019 29/05/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Image: Sector of the secto	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 27/05/2019 27/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 29/05/2019 29/05/2019 31/05/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Image: Source in the second secon	Start (PM) 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 27/05/2019 27/05/2019 30/05/2019 30/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 29/05/2019 29/05/2019 31/05/2019 31/05/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
SynAuzzas SynAuzzas	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 22/05/2019 30/05/2019 30/05/2019 30/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019 29/05/2019 31/05/2019 31/05/2019 07/06/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo				25		Jul
Isynwzens Isynwzens	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 27/05/2019 30/05/2019 30/05/2019 50/06/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019 29/05/2019 31/05/2019 31/05/2019 07/06/2019 07/06/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo		23		25		Jul
Evilence	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 22/05/2019 30/05/2019 30/05/2019 30/05/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019 29/05/2019 31/05/2019 31/05/2019 07/06/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo		23		25		Jul
Projet Demo Name (PM) Projet Demo Sous-projet par défaut Phase 1: Gitatoire Nord Sous-projet par défaut Phase 1: Gitatoire Nord Phase 1:	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 20/05/2019 30/05/2019 30/05/2019 05/06/2019 05/06/2019 07/06/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 24/05/2019 29/05/2019 31/05/2019 31/05/2019 07/06/2019 07/06/2019 07/06/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo		23		25		Jul
Evilence	Start (PM) 17/04/2019 17/04/2019 17/04/2019 17/04/2019 22/05/2019 22/05/2019 22/05/2019 27/05/2019 30/05/2019 05/06/2019 05/06/2019 05/06/2019	21/02/2020 21/02/2020 21/06/2019 03/05/2019 24/05/2019 29/05/2019 29/05/2019 31/05/2019 07/06/2019 07/06/2019		20/05/2019 17/04 Move then z	Apr			2019 May	Printed zo		23		25		Jul

Export the video

You can export the created video by clicking the Export Video button at the bottom left and then clicking Start. You will be able to modify the name of the video as well as the path where it will be saved on your PC. Set the quality of your video. The higher the quality, the more space the video will take up.

Projet Linéaire 12 impasse Bernard Lyot 85 000 LA ROCHE-SUR-YON Tél. : +33(0) 2 22 44 52 52 support@projetlineaire.com



😥 PhaseManager	😵 Enregistrer vidéo	_		_	ο×
	MP4				
		Titre :	Projet Demo		
2		Enregistrer dans :			Parcourir
		Qualité :	Léger Bonne	Elevée	Maximale
		Résolution :	1980x1080		
		Durée :	00:00:26		
		Taille du fichier :	13.631488 Mo		
					_
				Démarrer	Annuler
Montage Nouveau montage1 + - 🕒					
00.05 05 - 17/04/2015		00:10		00:15	
			17/04/2019 17/04/2019		
	Plan-	Zoomer	et Déplacer		
